Miller Driscoll School
Wilton, CT

2 Week Look Ahead

ID	Task Name	Duration	Start	Finish
1	**Two Week Look-Ahead**	**93 days**	**Mon 1/11/16**	**Fri 5/6/16**
2	**Sitework**	**70 days**	**Mon 1/11/16**	**Tue 4/5/16**
3	Excavate / Backfill for New Foundations	56 days	Mon 1/11/16	Fri 3/18/16
4	Excavate / Backfill for New Utilities at Column Line 14 thru 24	22 days	Mon 3/7/16	Thu 3/31/16
5	Placement of Fill Material at New Bus Loop	25 days	Mon 3/7/16	Tue 4/5/16
6	Relocate Fence at Miller and Install Gate Adjacent to Temp. Classrooms	2 days	Tue 3/15/16	Wed 3/16/16
7	Install Gravel Access Path Around Back of Site	10 days	Thu 3/17/16	Mon 3/28/16
8	**Concrete**	**66 days**	**Wed 1/13/16**	**Fri 4/1/16**
9	Formwork at Pre-K Foundations	40 days	Wed 1/13/16	Wed 3/2/16
10	Install Rebar at Pre-K Foundations	40 days	Thu 1/14/16	Thu 3/3/16
11	Pour Foundations at Pre-K Wing	38 days	Tue 1/19/16	Fri 3/4/16
12	Foundations at Column Line 14 thru 24	42 days	Mon 2/8/16	Mon 3/28/16
13	Pour Slab on Grade at Pre-K Wing	3 days	Wed 3/30/16	Fri 4/1/16
14	**Structural Steel**	**25 days**	**Mon 4/4/16**	**Fri 5/6/16**
15	Installation of Structural Steel (Column Line 14-24)	20 days	Mon 4/4/16	Fri 4/29/16
16	Installation of Structural Steel (Column Line 14-24)	20 days	Mon 4/11/16	Fri 5/6/16
17	**Mechanical, Electrical, & Plumbing (MEP's)**	**71 days**	**Wed 1/27/16**	**Fri 4/22/16**
18	Install Underground Plumbing at Pre-K Wing	25 days	Wed 1/27/16	Wed 2/24/16
19	Install Undergound Electrical at Pre-K Wing	20 days	Mon 2/1/16	Tue 2/23/16
20	Install Underground MEPs Column Line 14 thru 24	22 days	Tue 3/8/16	Fri 4/1/16
21	Install Incoming MEPs	27 days	Sat 3/19/16	Fri 4/22/16
22	**Miller Storage Area Renovation**	**1 day**	**Mon 4/4/16**	**Mon 4/4/16**
23	Demolition of Walls & Ceilings	1 day	Mon 4/4/16	Mon 4/4/16

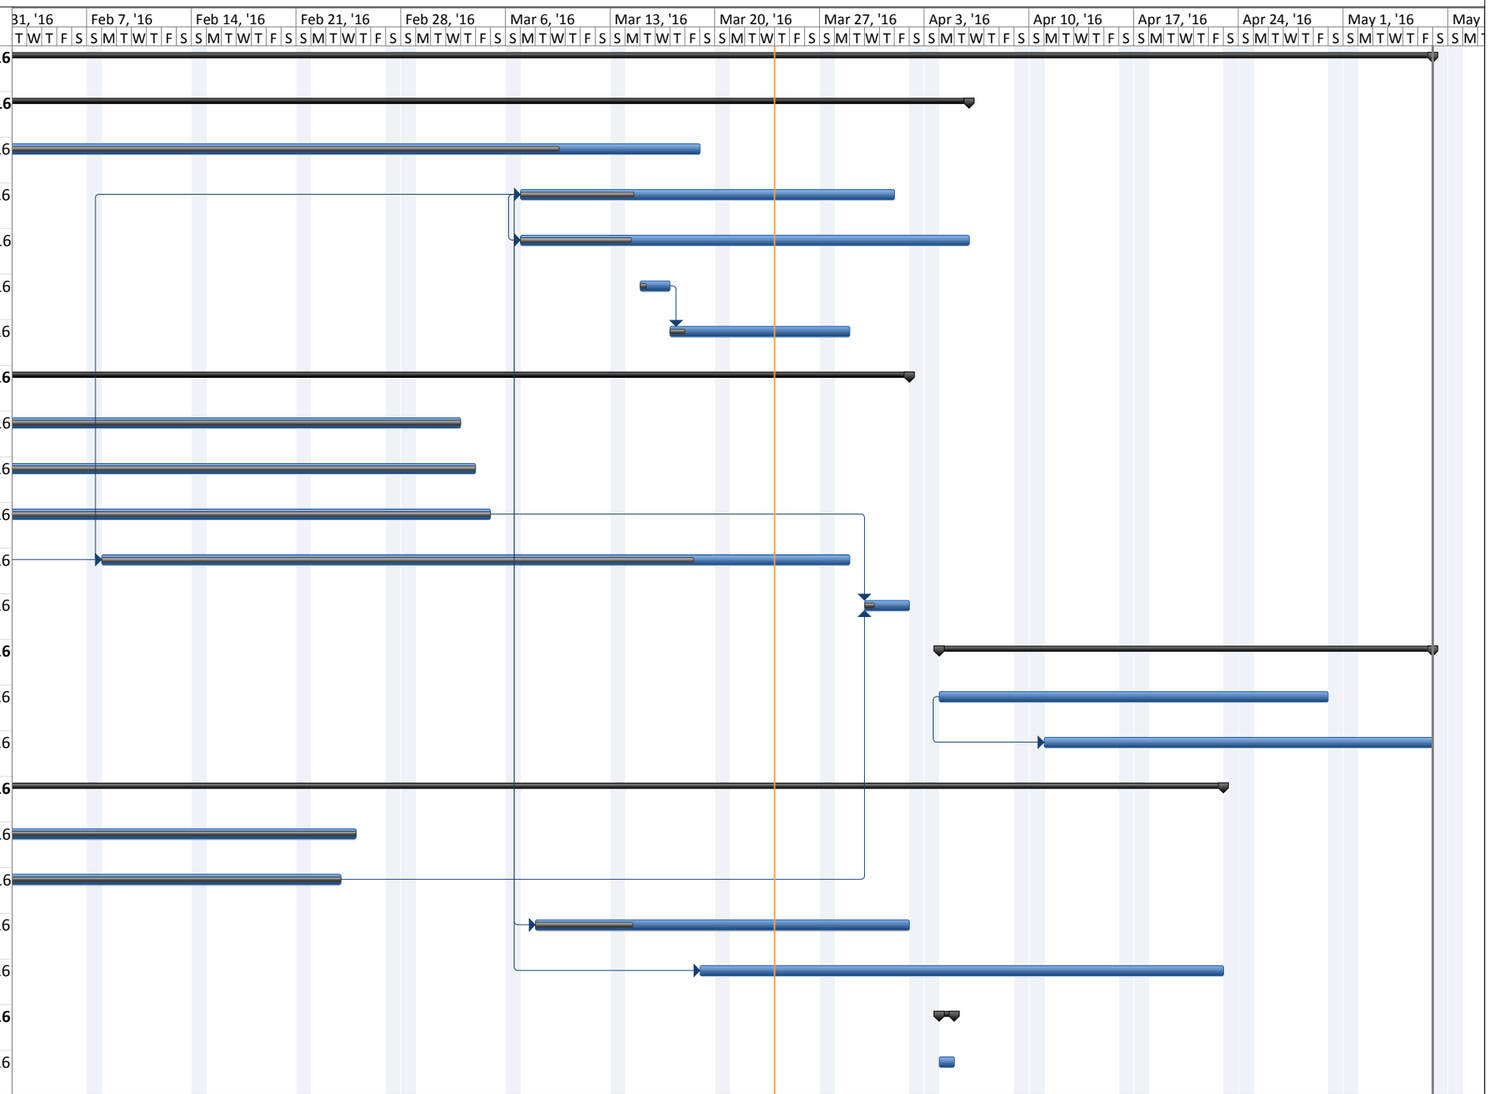

Project: 03-21-16 2 Week Look Ah
Date: Thu 3/24/16

Task	Summary	External Milestone	Inactive Summary	Manual Summary Rollup	Finish-only		
Split	Project Summary	Inactive Task	Manual Task	Manual Summary	Deadline		
Milestone	External Tasks	Inactive Milestone	Duration-only	Start-only	Progress		
